

Portfolio

All projects, one screen. Scores use the same weights and bands as the Scorecard page. A category with no data

19

Proiects Reporting

\$35M

Current Contract

63.0%

Total Billed %

\$7M


AR Outstanding

6

Proiects At Risk

| ProjectName                                                | Cash Position | Change Orders | Observations | Safety |
|------------------------------------------------------------|---------------|---------------|--------------|--------|
| 11 ESSEX ST                                                |               | 0             | 0            |        |
| 1100 Fulton Street                                         |               | 0             | 0            |        |
| 337A & 337B West Broadway Rehabilitaion Work               |               |               |              |        |
| 360 Lexington 8th & 20th Floor                             |               |               | 0            |        |
| 549 Munroe Av                                              |               |               |              |        |
| 64 MET OVAL PSC + 1410 MET STOREROOM                       |               |               | 0            |        |
| Boys & Girls Club                                          |               |               |              |        |
| City Harvest                                               |               |               |              |        |
| Embankment + Revetment Apartments 270 & 310 10th Street NJ |               | 0             | 2            |        |
| EMBANKMENT PHASE II                                        |               | 3             | 0            |        |
| Embankment Phase III                                       |               | 3             |              |        |
| Total                                                      | 3             | 0             | 0            |        |


Contract, billed and paid by project

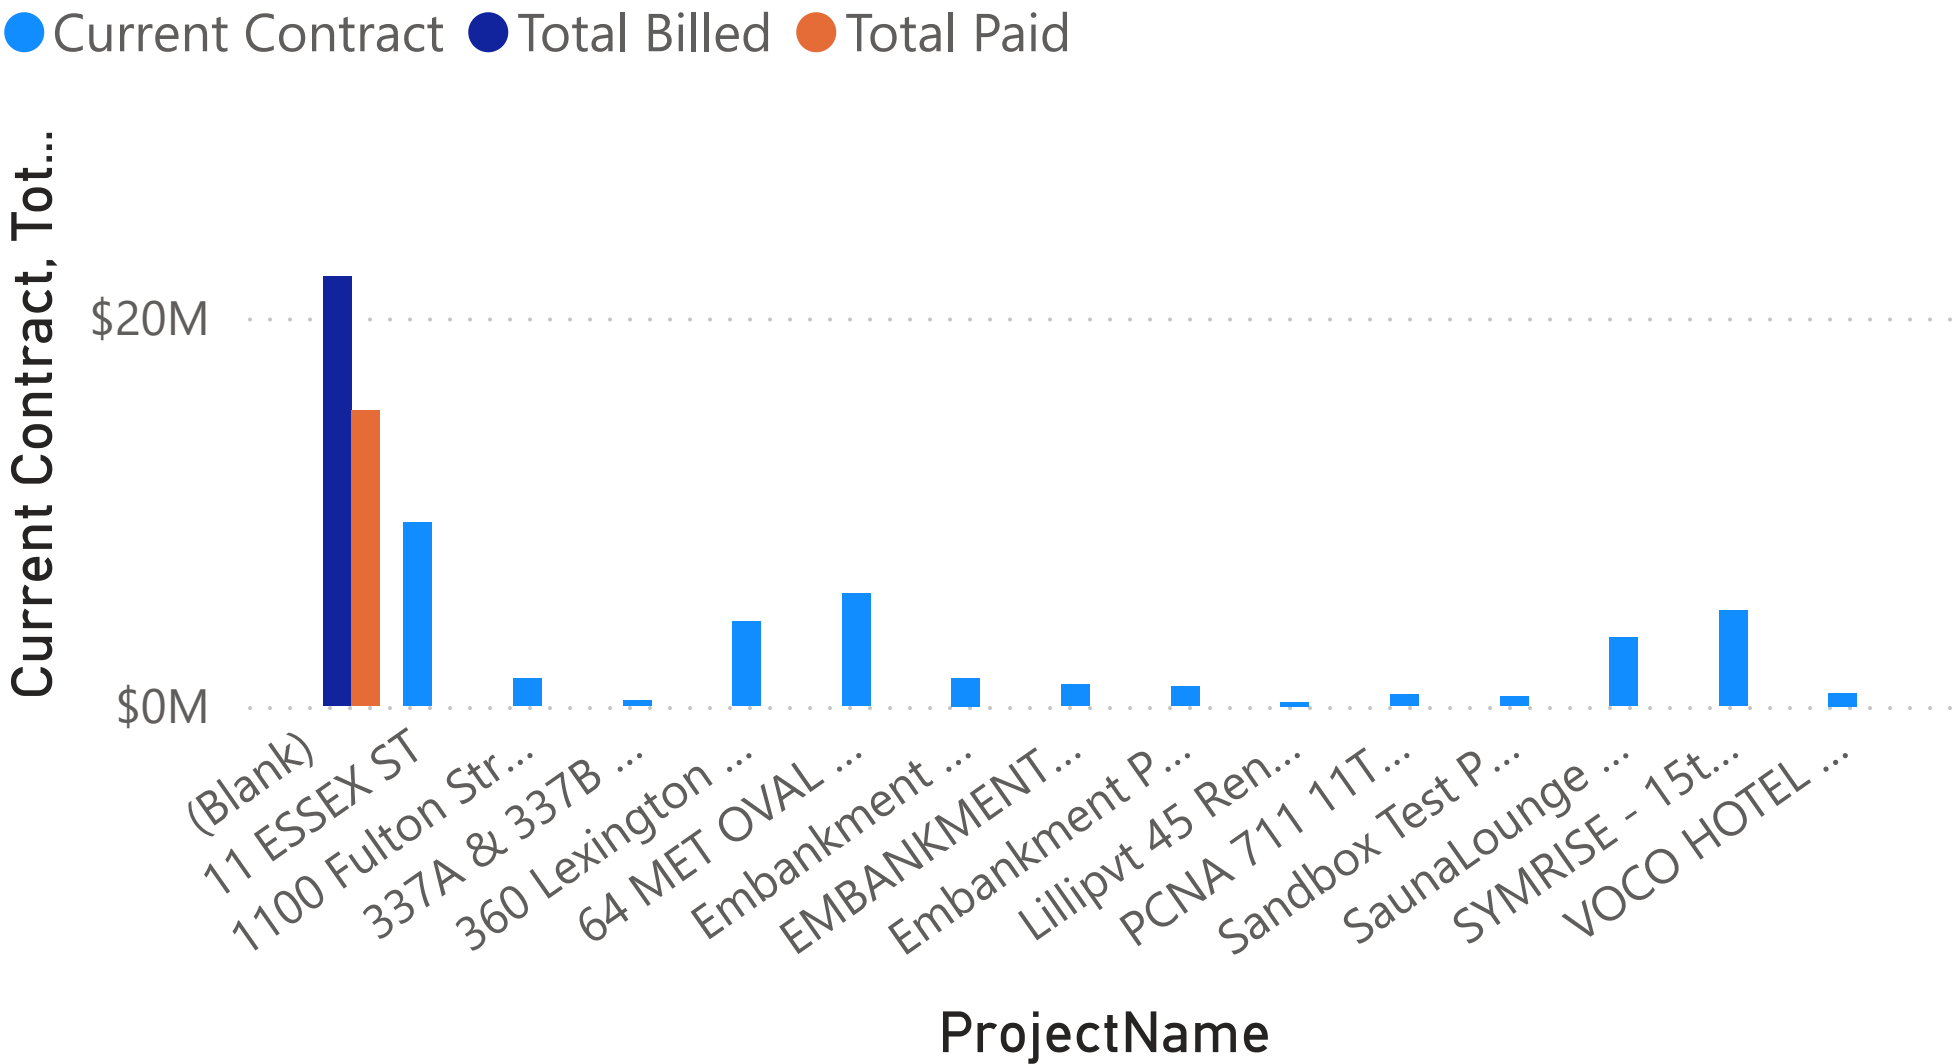

AR outstanding, ranked



Scorecard coverage by project

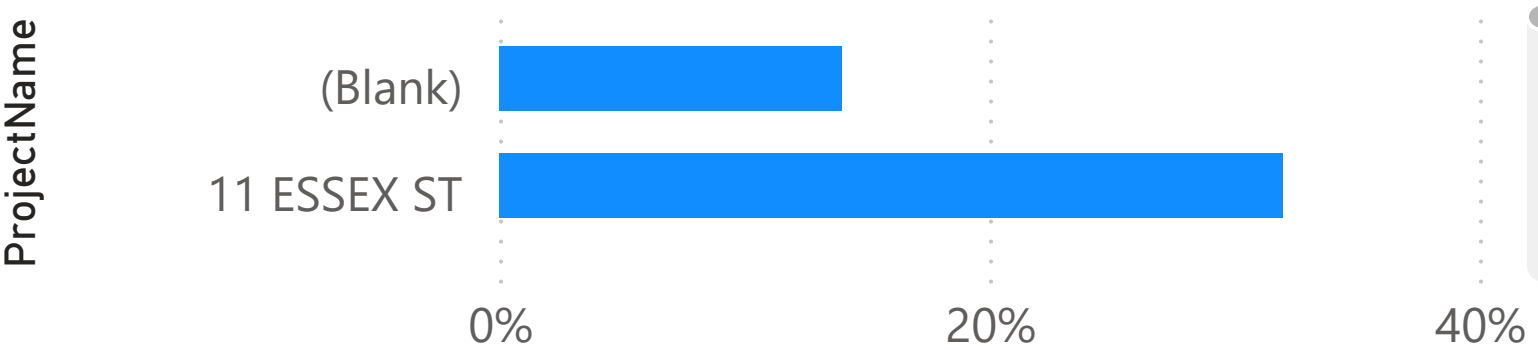

Vendors with no certificate on file, by project



# Monthly Progress Report

Replaces the Excel Monthly Progress Report

ProjectName

(Blank)

MonthYear

(Blank)

\$35M

Current Contract

\$22M

Total Billed

63.0%

Total Billed %

\$15M

Total Paid

\$7M

AR Outstanding

16.03%

Contract Growth %

86.5%

Percent Bought Out

\$59K

Pending Change Orders


2,189

Open Submittals

52


Critical Milestones

Billed by month

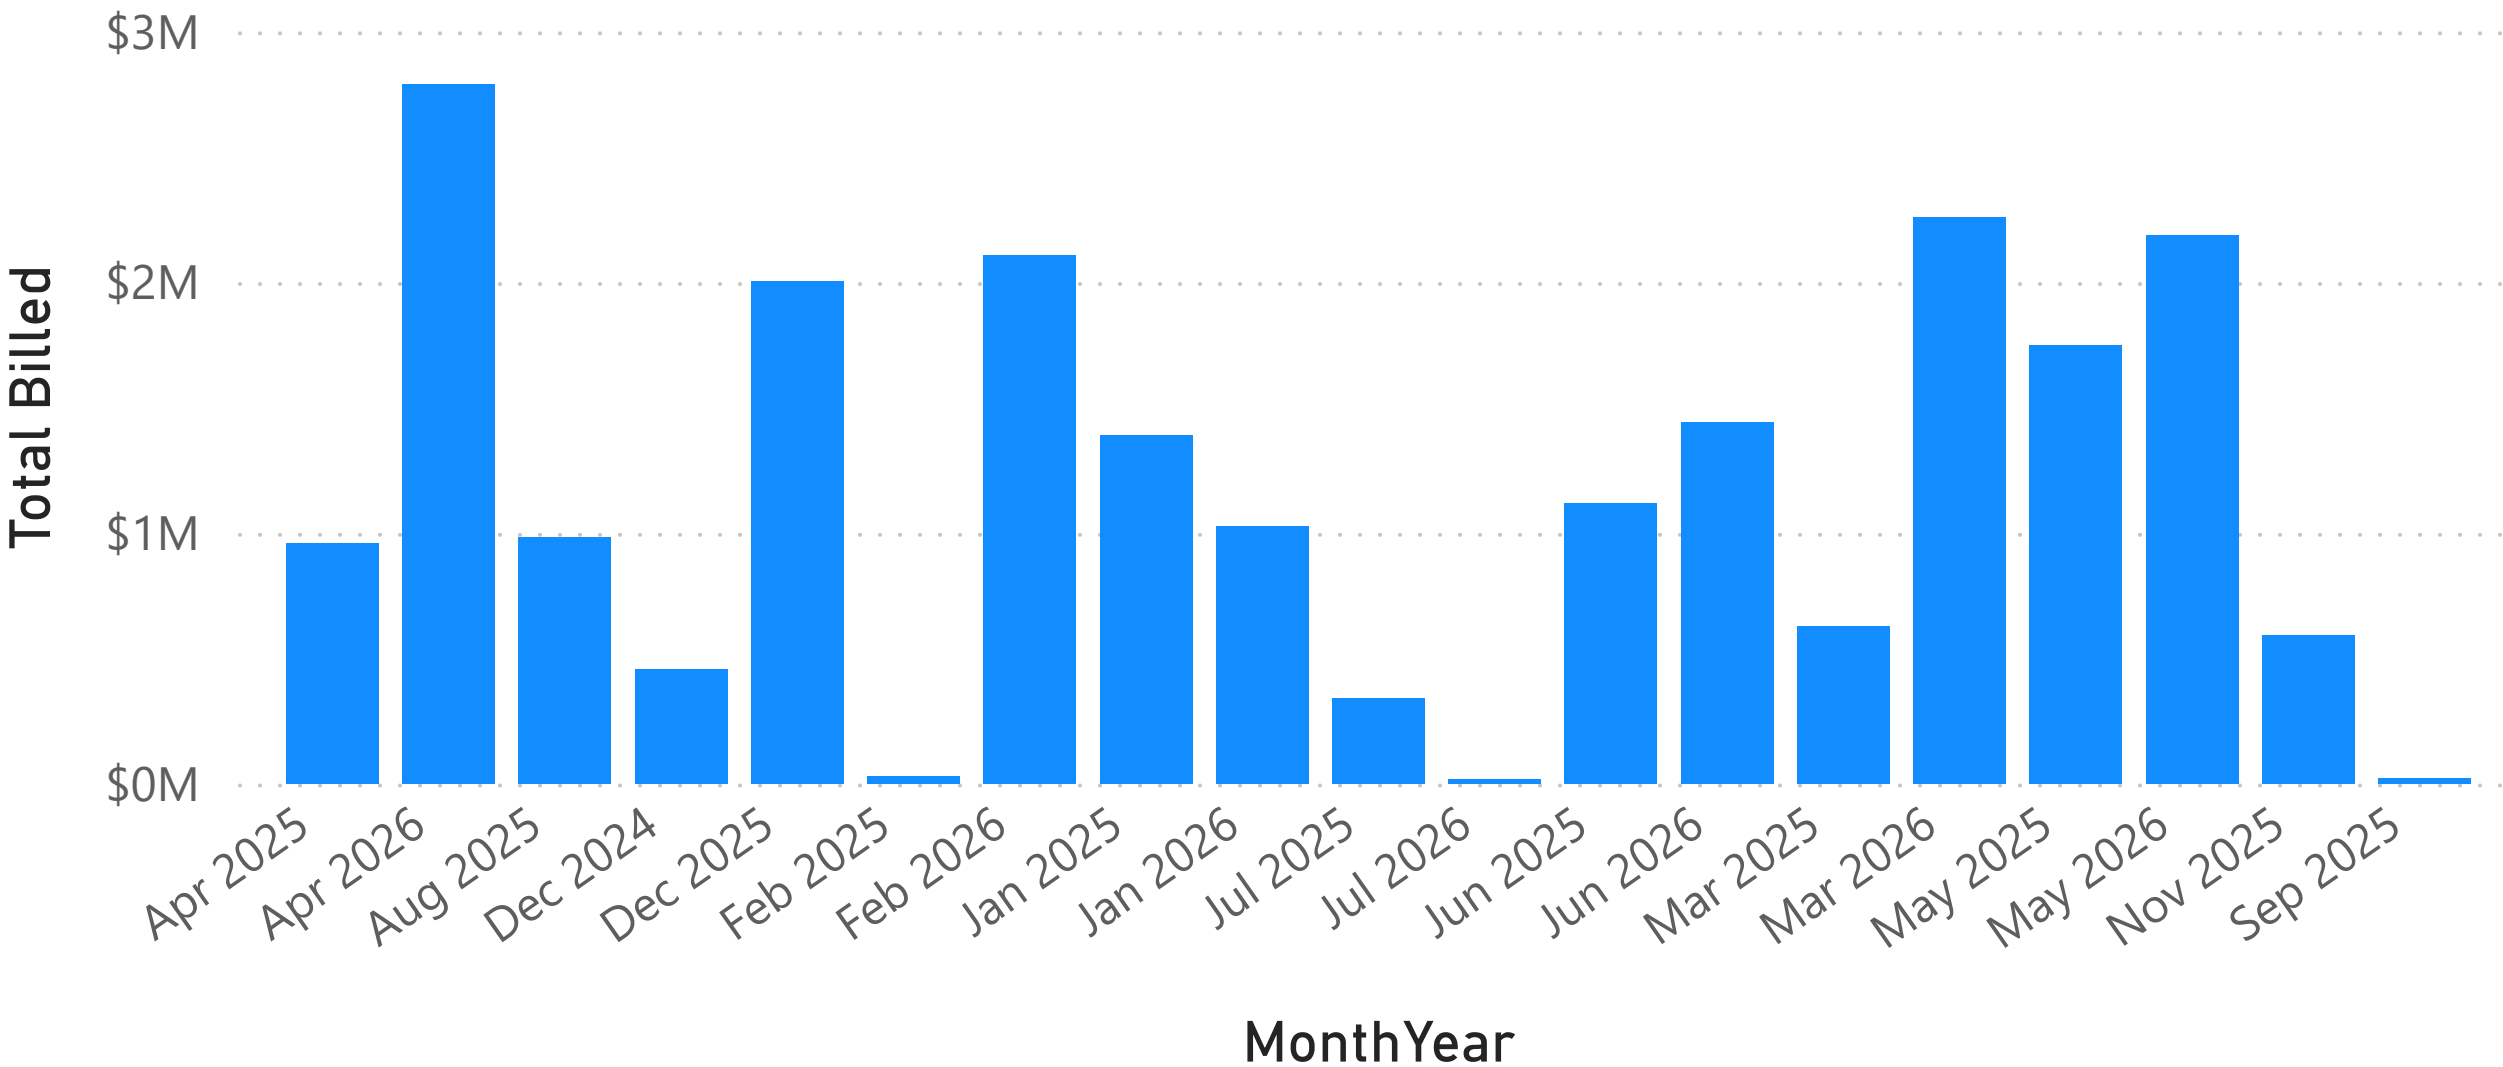

Budget vs spent by division

Budget Spent To Date

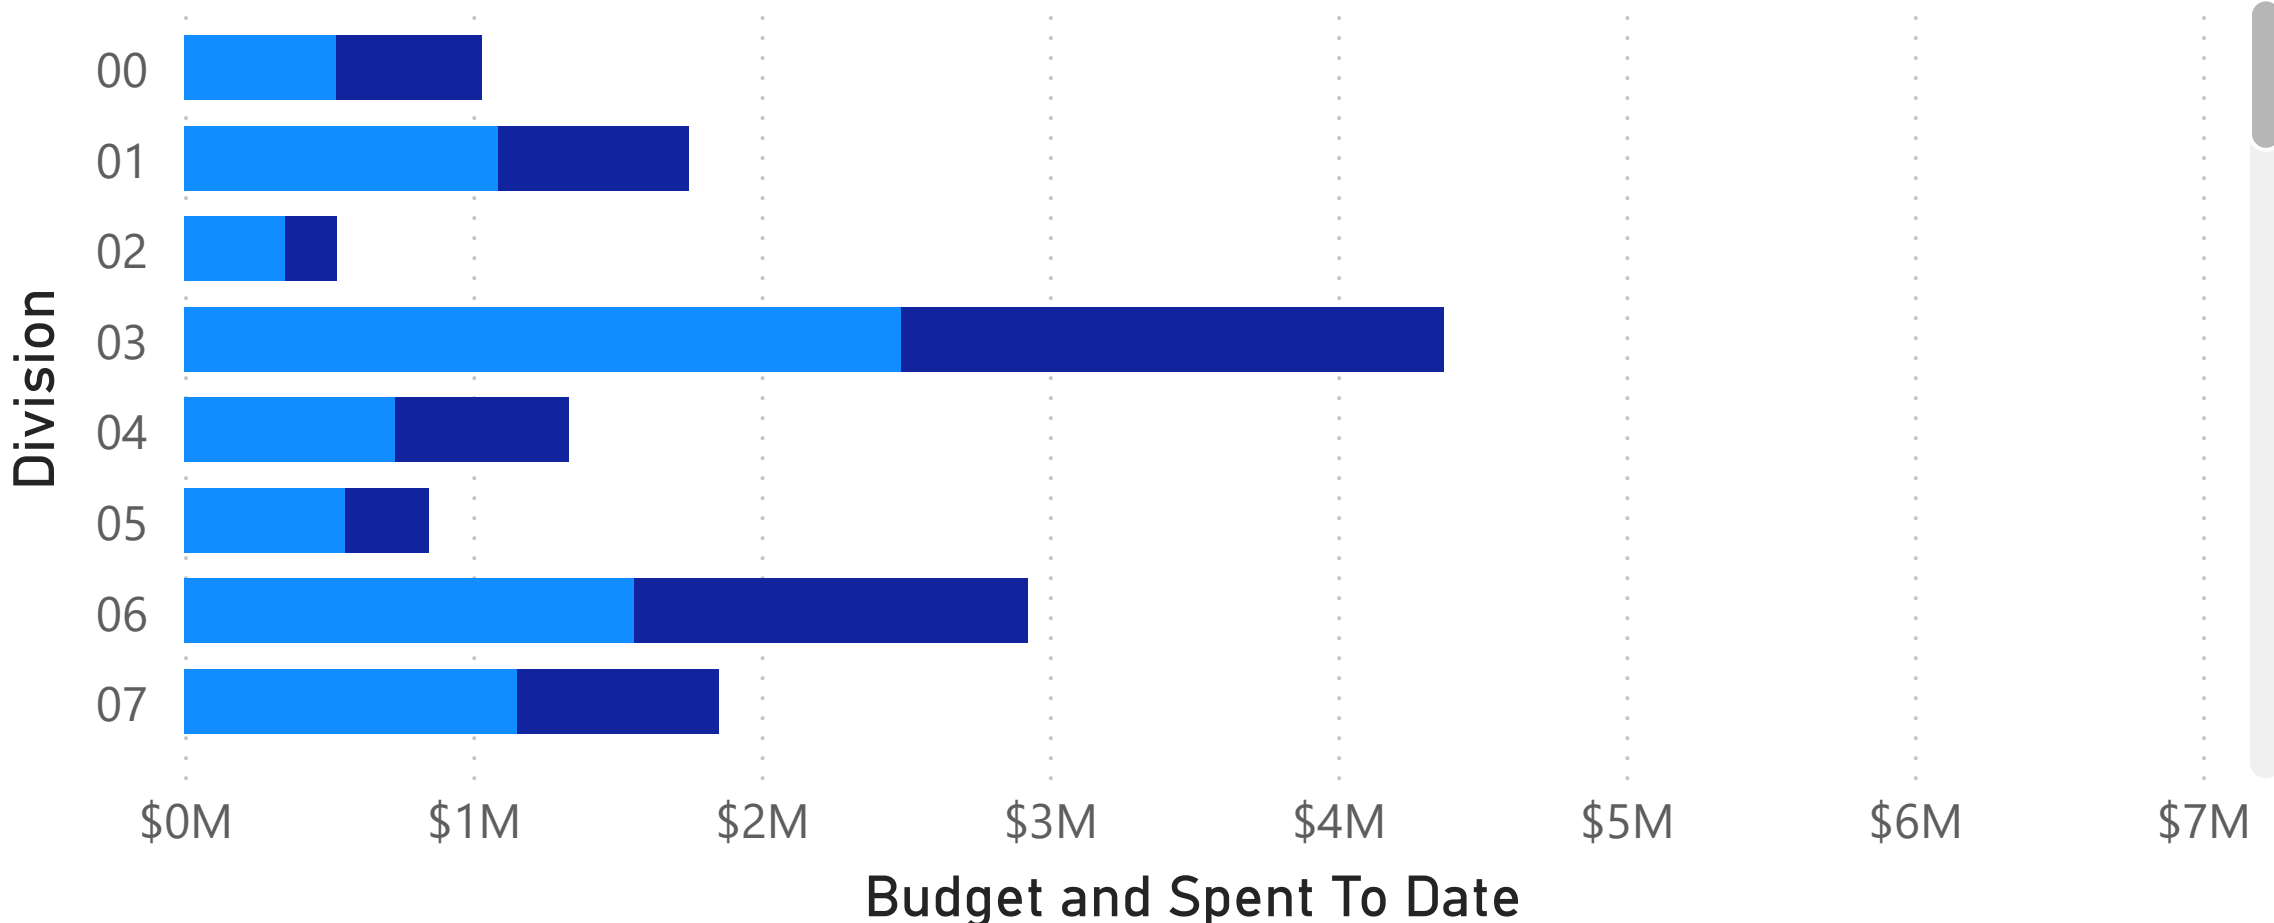

January 2015 - Dec...  
Report Month Label

2026-08-03 06:06  
Last Refresh

Current  
Pipeline Status



Financial

ProjectName

(Blank)

MonthYear

(Blank)

\$34M

Budget

\$34M

Forecast

\$29M

Committed

\$19M

Spent To Date

\$11M


Cost To Complete

\$15M


Budget Variance

| Division | Budget       | Spent To Date | Budget Variance | Budget Variance % | Budget Status |
|----------|--------------|---------------|-----------------|-------------------|---------------|
| + 00     | \$526,592    | \$504,495     | \$22,098        | 4.2%              | On Track      |
| + 01     | \$1,089,447  | \$660,381     | \$429,066       | 39.4%             | On Track      |
| + 02     | \$351,011    | \$180,002     | \$171,009       | 48.7%             | On Track      |
| + 03     | \$2,487,064  | \$1,881,757   | \$605,307       | 24.3%             | On Track      |
| + 04     | \$731,348    | \$601,596     | \$129,752       | 17.7%             | On Track      |
| + 05     | \$560,124    | \$290,809     | \$269,315       | 48.1%             | On Track      |
| + 06     | \$1,562,808  | \$1,365,871   | \$196,937       | 12.6%             | On Track      |
| + 07     | \$1,154,378  | \$700,652     | \$453,727       | 39.3%             | On Track      |
| + 08     | \$1,326,067  | \$561,687     | \$764,380       | 57.6%             | On Track      |
| + 09     | \$3,949,110  | \$2,754,632   | \$1,194,478     | 30.2%             | On Track      |
| + 1      | \$1,284,833  | \$42,792      | \$1,242,041     | 96.7%             | On Track      |
| + 10     | \$559,037    | \$239,978     | \$319,059       | 57.1%             | On Track      |
| + 11     | \$369,457    | \$142,090     | \$227,367       | 61.5%             | On Track      |
| + 12     | \$71,309     | \$26,029      | \$45,280        | 63.5%             | On Track      |
| + 14     | \$1,435,266  | \$949,489     | \$485,777       | 33.8%             | On Track      |
| + 15     | \$1,099,748  | \$95,000      | \$1,004,748     | 91.4%             | On Track      |
| + 16     | \$678,717    | \$45,916      | \$632,801       | 93.2%             | On Track      |
| + 17     | \$517        | \$0           | \$517           | 100.0%            | On Track      |
| + 2      | \$192,845    | \$0           | \$192,845       | 100.0%            | On Track      |
| Total    | \$33,873,972 | \$18,568,853  | \$15,305,120    | 45.2%             | On Track      |

Change orders by status

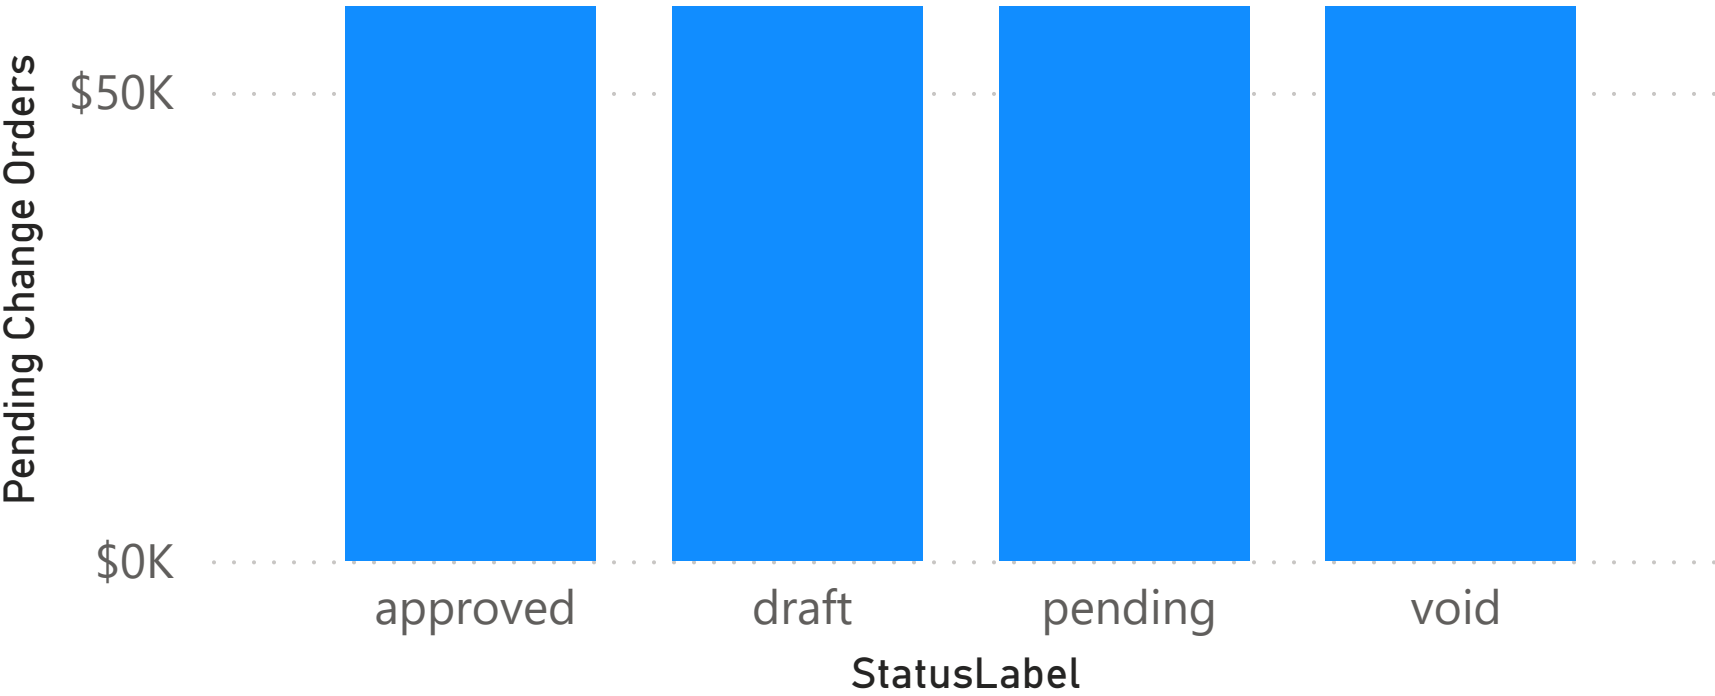

Billing S-curve vs contract

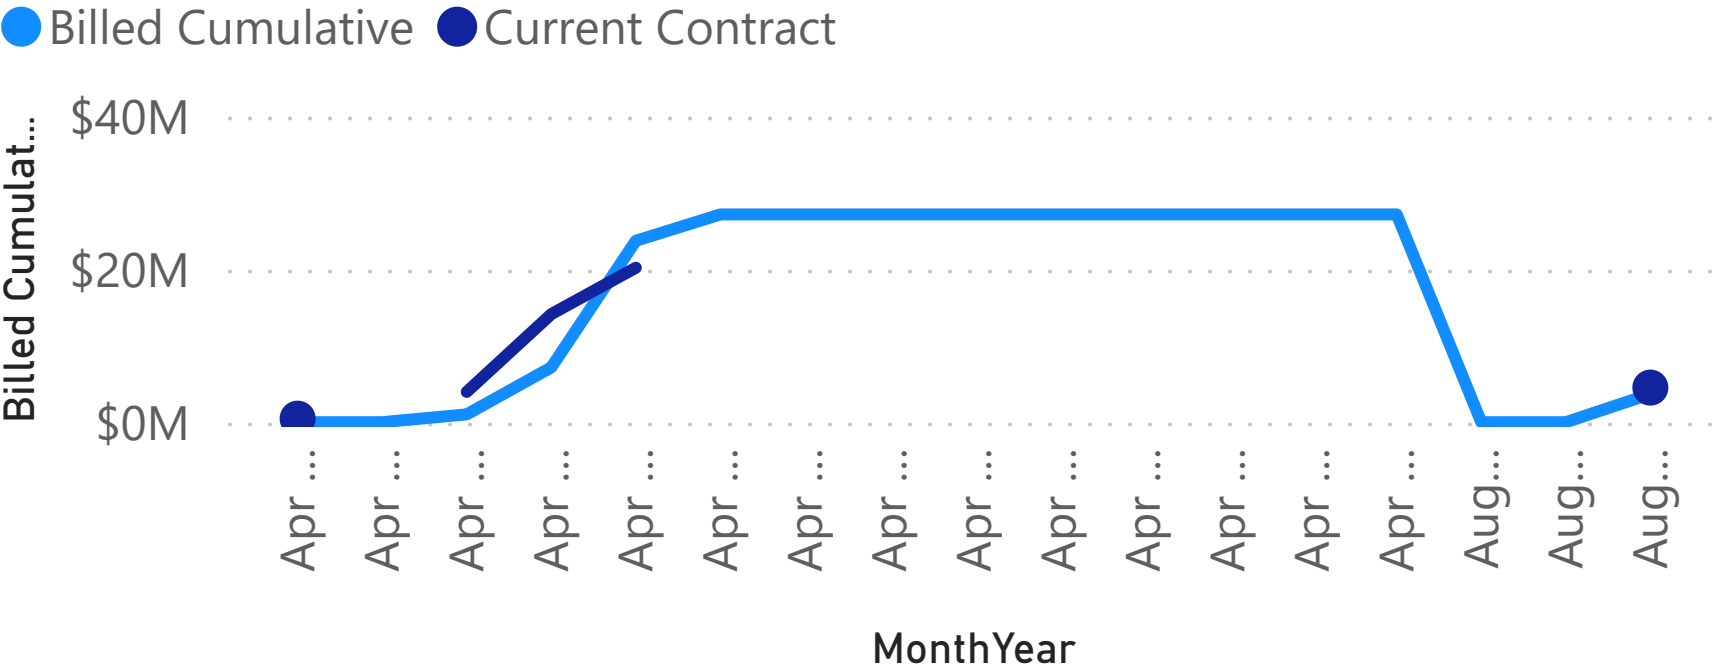

Schedule & Quality

ProjectName

(Blank)

MonthYear

(Blank)

52

Critical Milestones

31

Overdue Milestones

59.6%

Schedule Performance...

11.2%

Avg Milestone Progress

2,189

Open Submittals


49

Open Submittals Past ...



This visual does not support exporting.

Open submittals by status

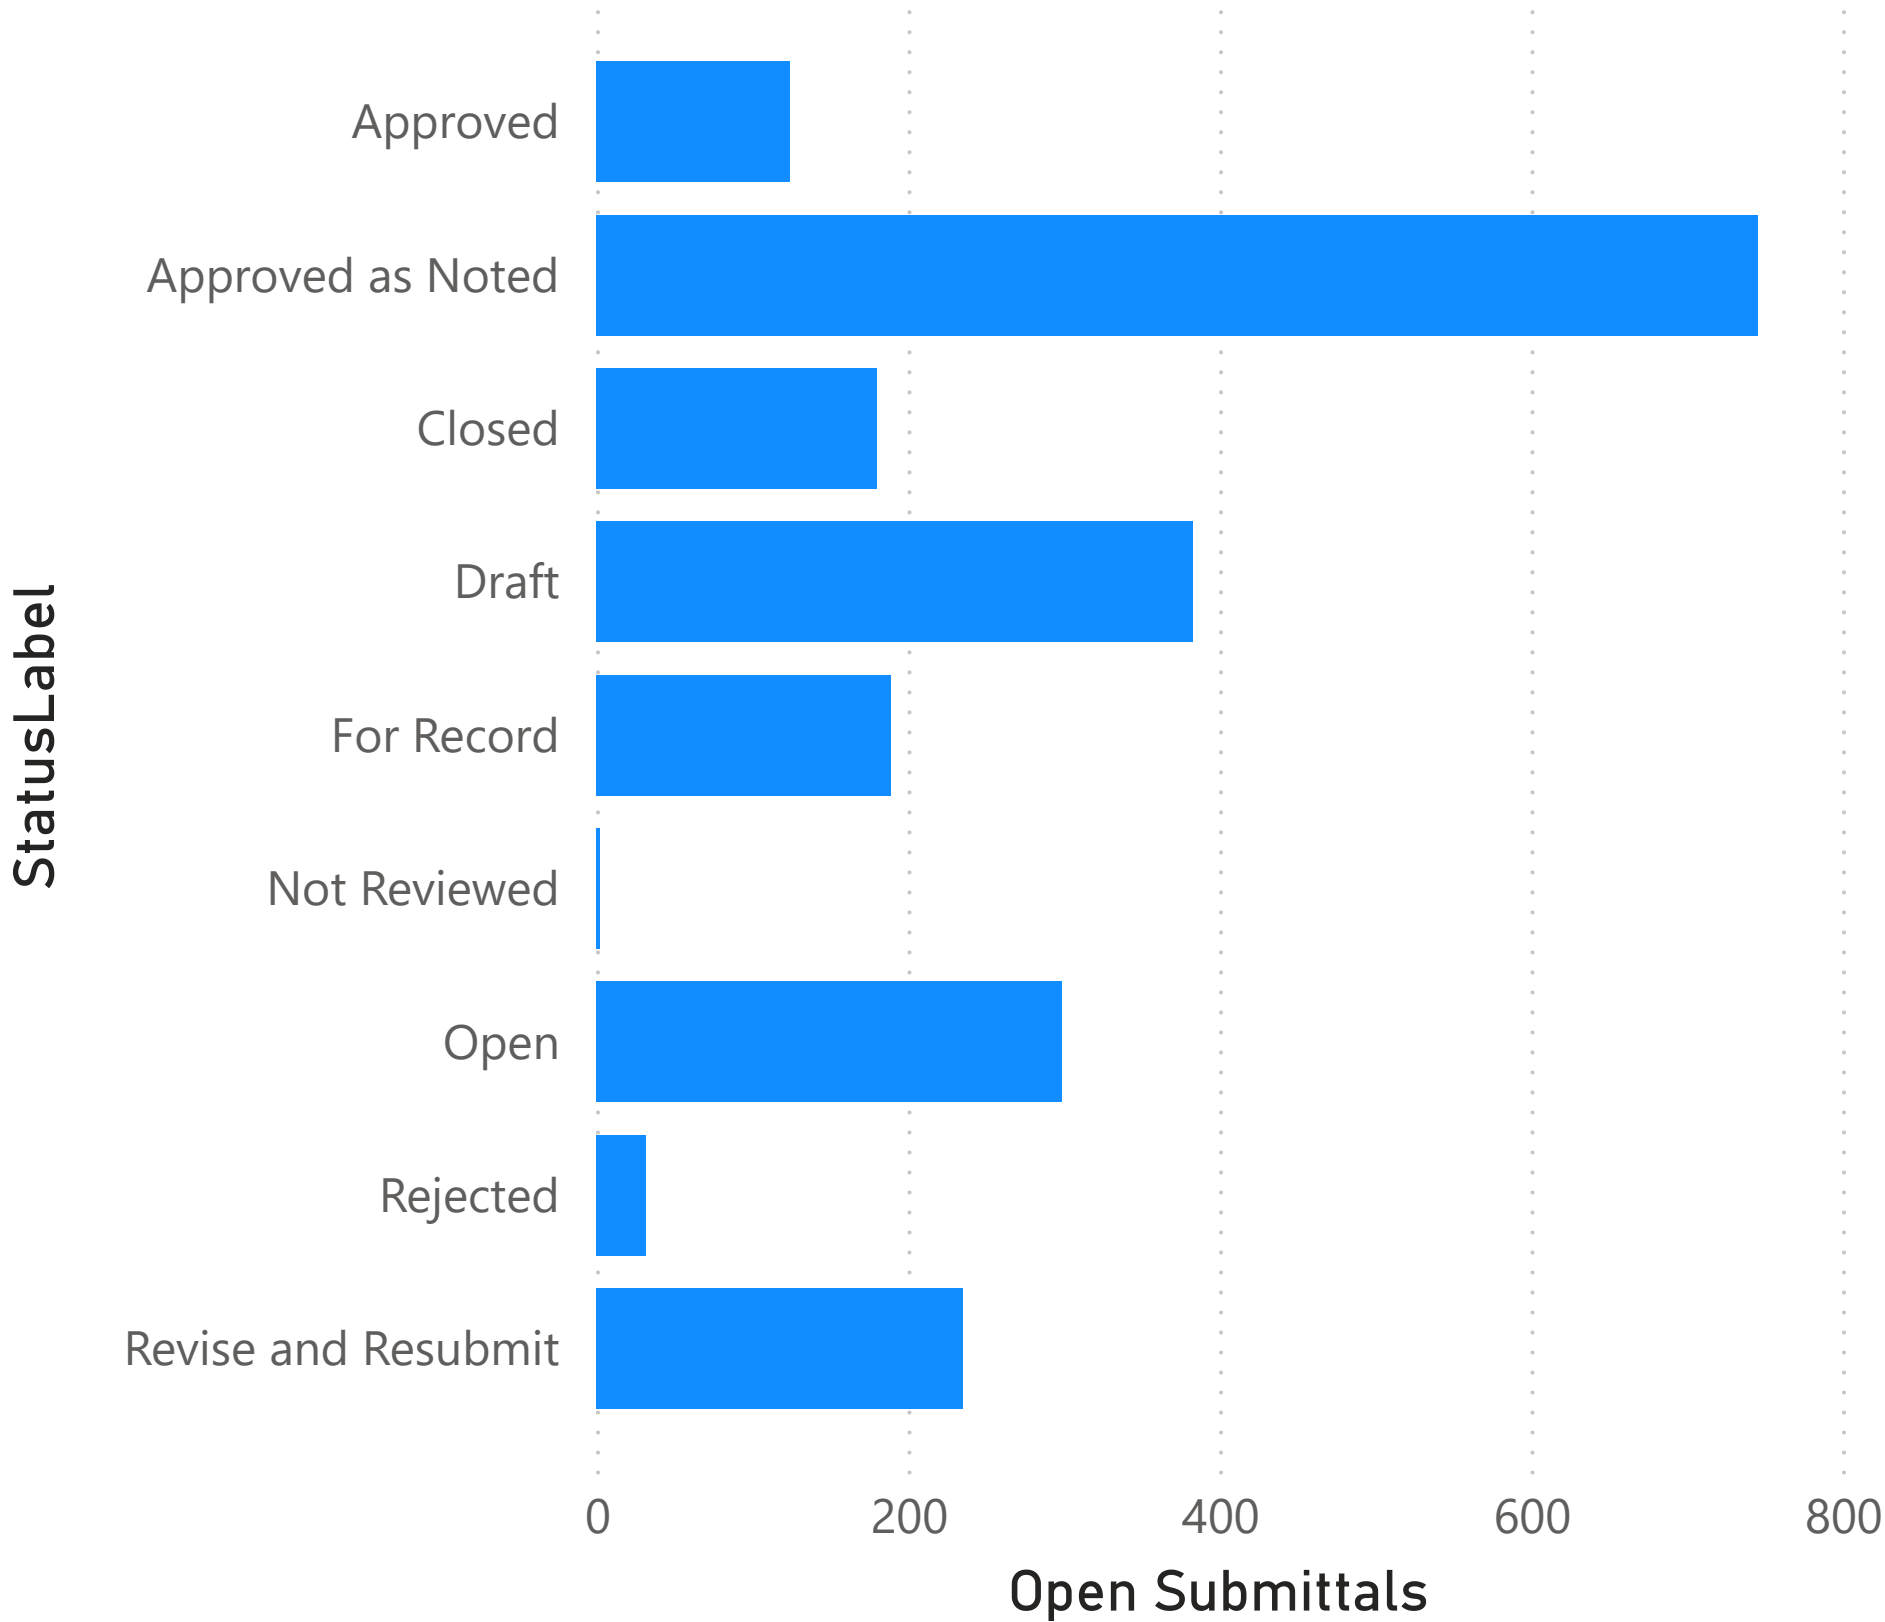

| MilestoneName             | CurrentStart | CurrentFinish | PercentComplete | StatusLabel          |
|---------------------------|--------------|---------------|-----------------|----------------------|
| 360Lex 15th & 17th Suites | 2026-06-10   | 2026-11-09    | 0.00            | No Float - High Risk |
| 360Lex 8th & 20th Suite   | 2025-12-26   | 2026-06-15    | 0.18            | Delayed              |
| 360Lex 8th & 20th Suite   | 2025-12-26   | 2026-06-24    | 0.80            | Delayed              |
| 360Lex 8th Amenity        | 2025-12-23   | 2026-06-15    | 0.25            | Delayed              |
| 360Lex 8th Amenity        | 2025-12-23   | 2026-06-15    | 0.25            | Delayed              |



# Safety & Quality

Every figure is counted from Procore records - observations, punch items, incidents and manpower logs - rather than typed each month. Status is shown as text, never

Safety

121K

Hours Worked

0

Recordable Incidents

Quality

850

Observations

1,469

Punchlist Items

108

Open Quality Items

104

Quality Items Past Due


195.2

Avg Days Past Due


30.9

Avg Observation Days Open

Open items by type

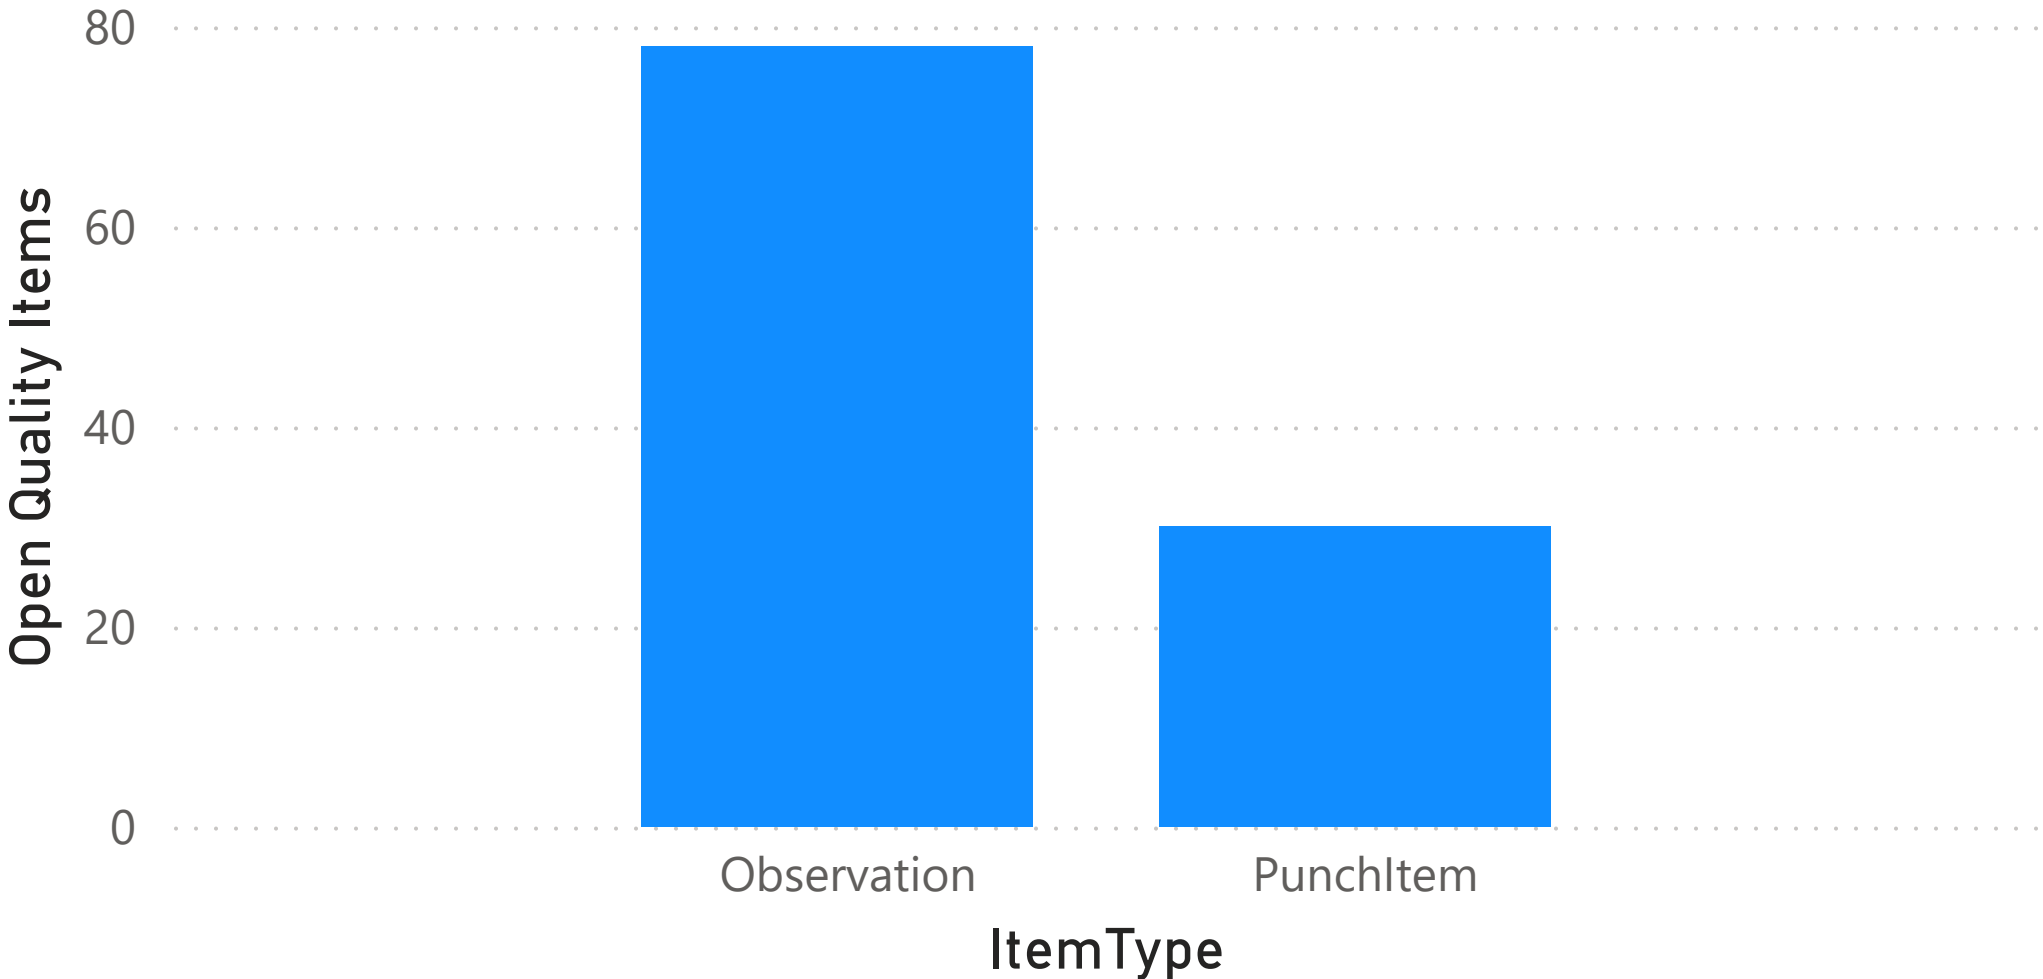

Open items by trade

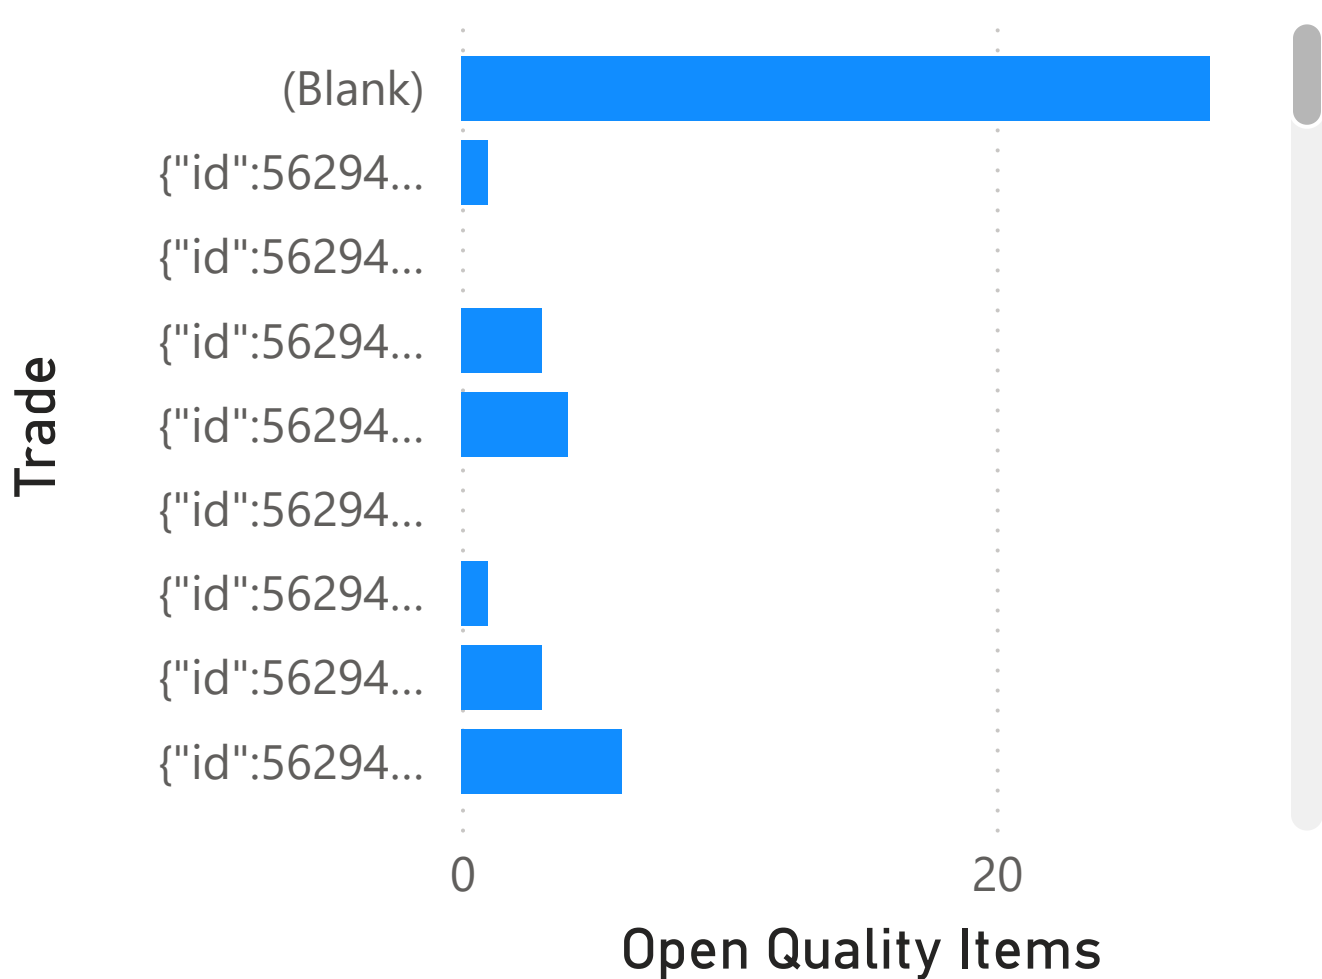

Title

- 1/4" Gap in height in tiles on 7th floor. Replace as needed
- 1410 Concrete Pour, Cylinder Inspection Report
- 1410 VRF QA/QC: AC ELEVATOR / CU-2
- 1410 VRF QA/QC: AC-1,2,4,6,7
- 1410 VRF QA/QC: AC-8
- 1410 VRF QA/QC: BC-1
- 1410 VRF QA/QC: CU-1
- 19th Floor - Patching Required [20th Floor Polishing Works]
- 1st Fl Overhead Rough



# Billing & Retainage

Every figure is the CURRENT balance from the latest issued billing per contract - not a total of every period, which would count the same retainage once per month. Drafts are excluded from

Retainage

Owner billina

\$345K

Net Retainage Position

\$831K

Retainage Held Owner

\$486K

Retainage Held Sub

\$34M

Owner Contract Sum

\$28M

Owner Billed To Date

\$7M

Balance To Finish


\$27M

Billed This Period


25

Draft Billinas

Billed by month (period movement, not cumulative)

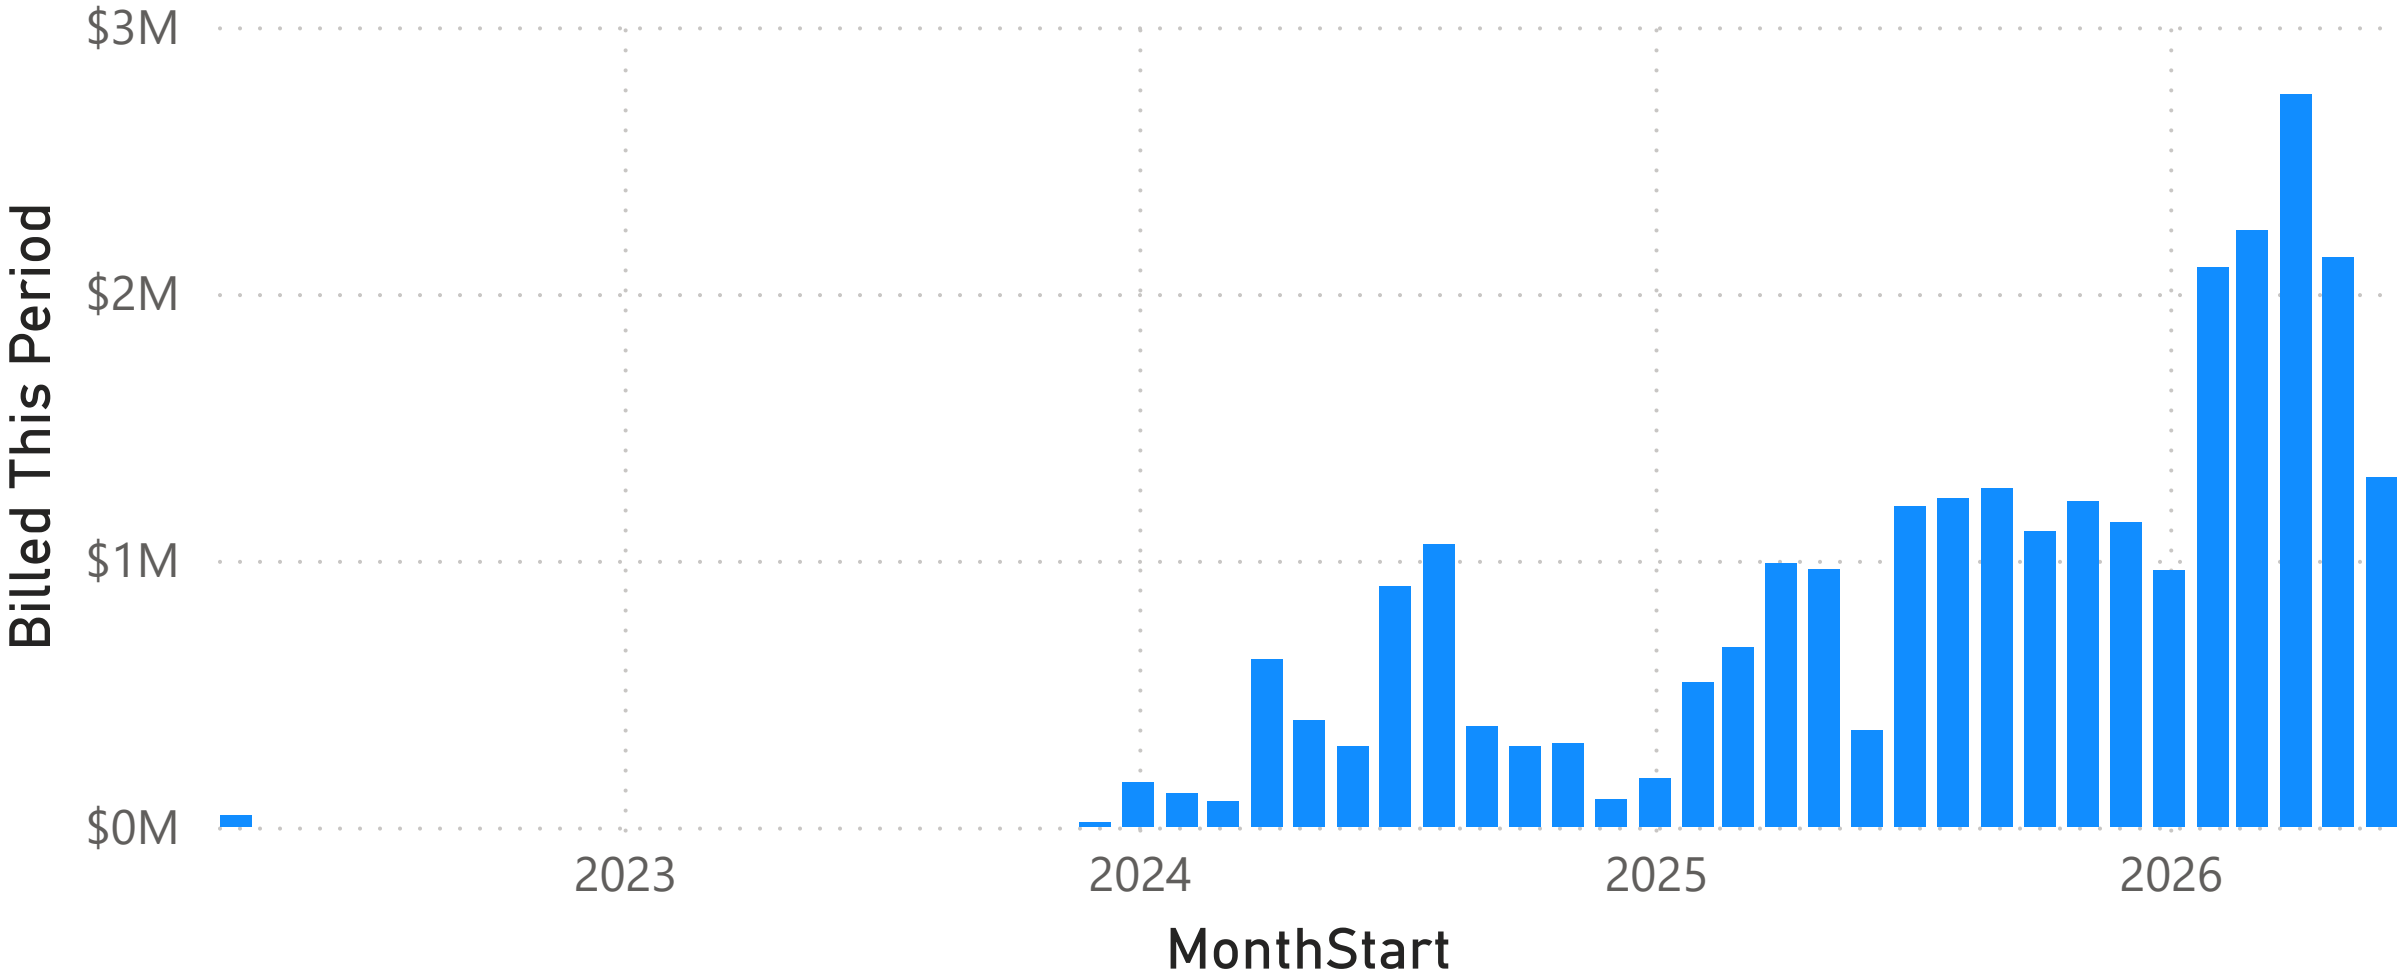

Retainage held by project

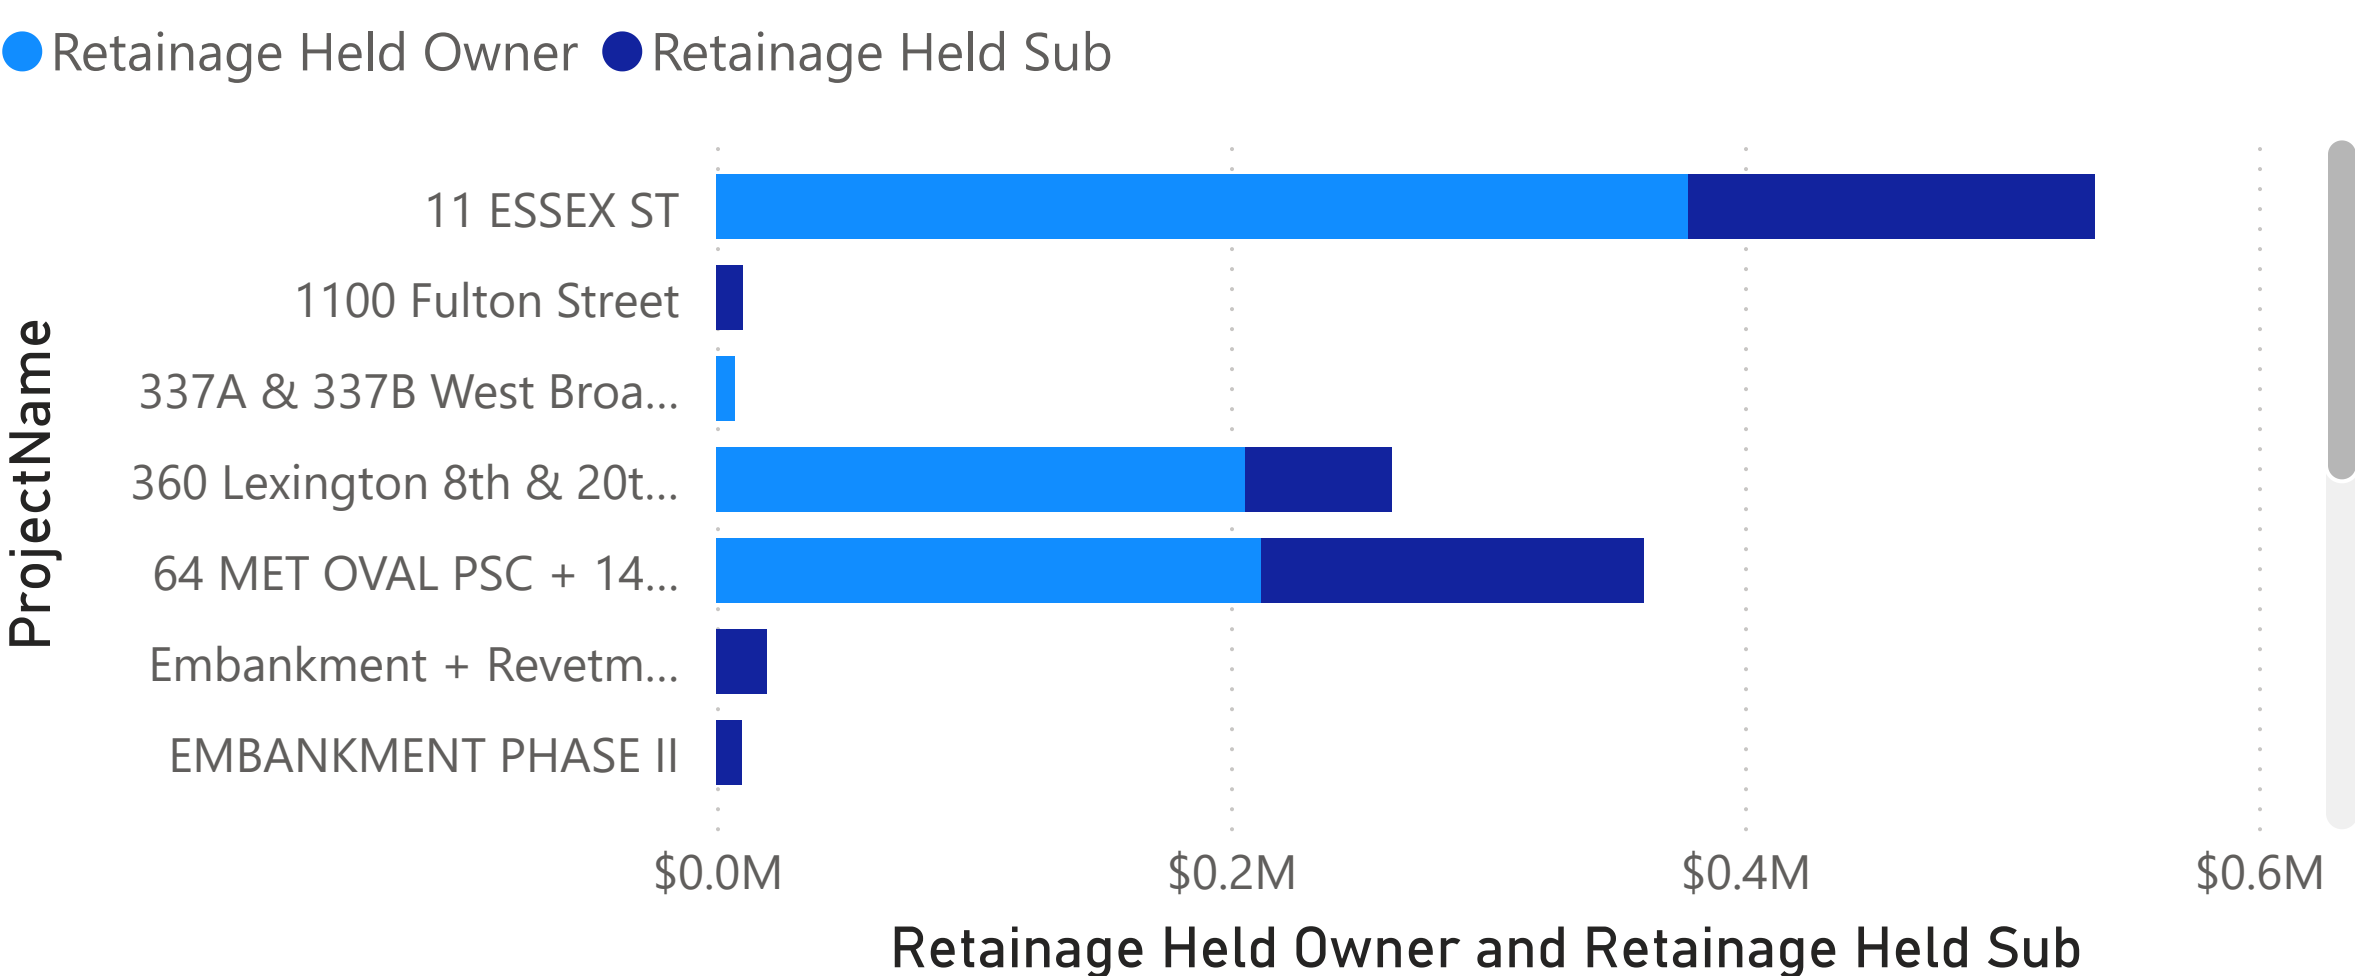

Direct Costs & Vendors

Direct costs are discrete transactions, so unlike the billing balances these totals are correct at any grouping. The vendor list is Procore's prequalification record, which is not the same as current

\$2M

Direct Costs

\$1M

Self Performed Labour

\$33K

Unapproved Direct Costs

251

Vendors On Project


125

Vendors Missing From F


\$26M

Vendor Committed


Direct cost by category

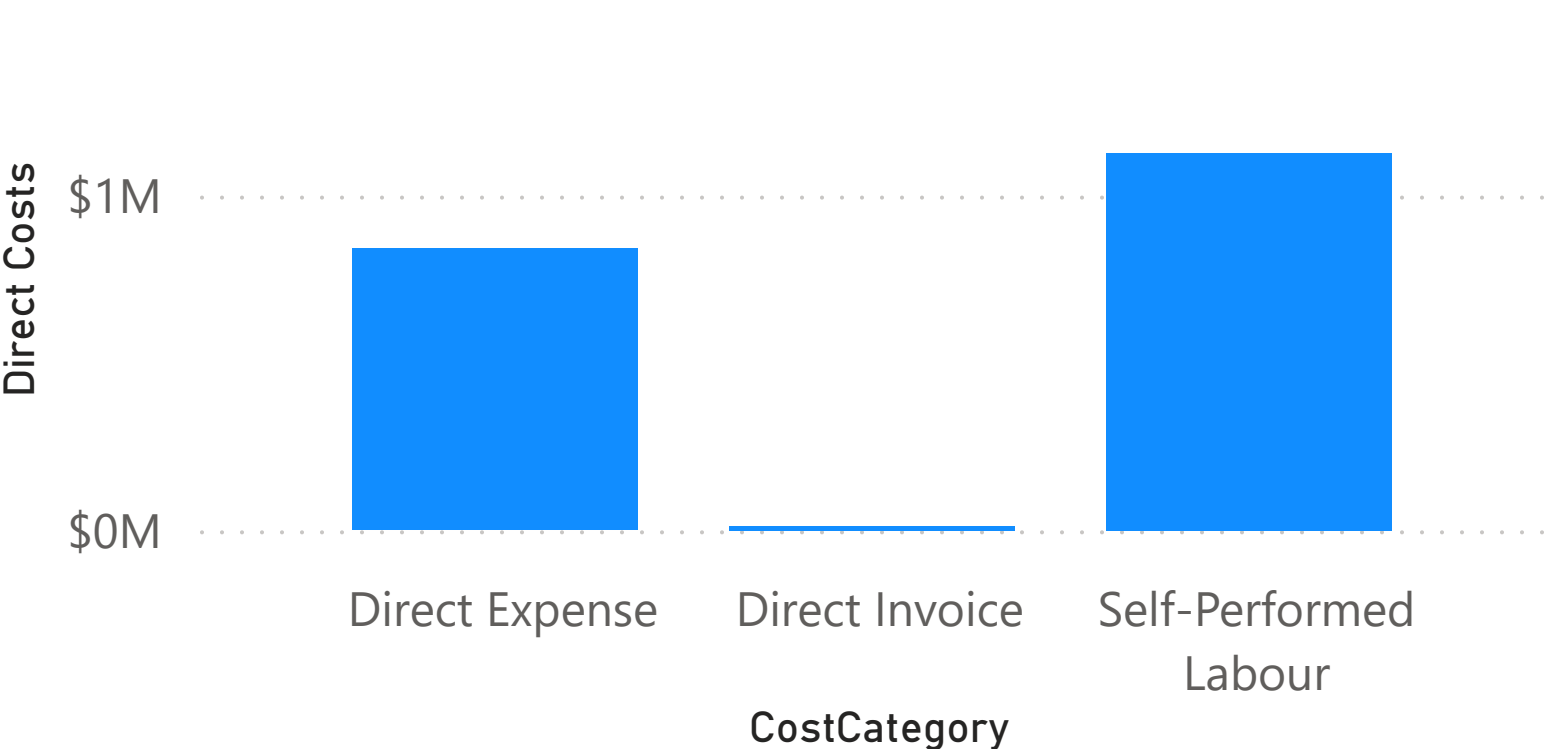

Direct cost by month

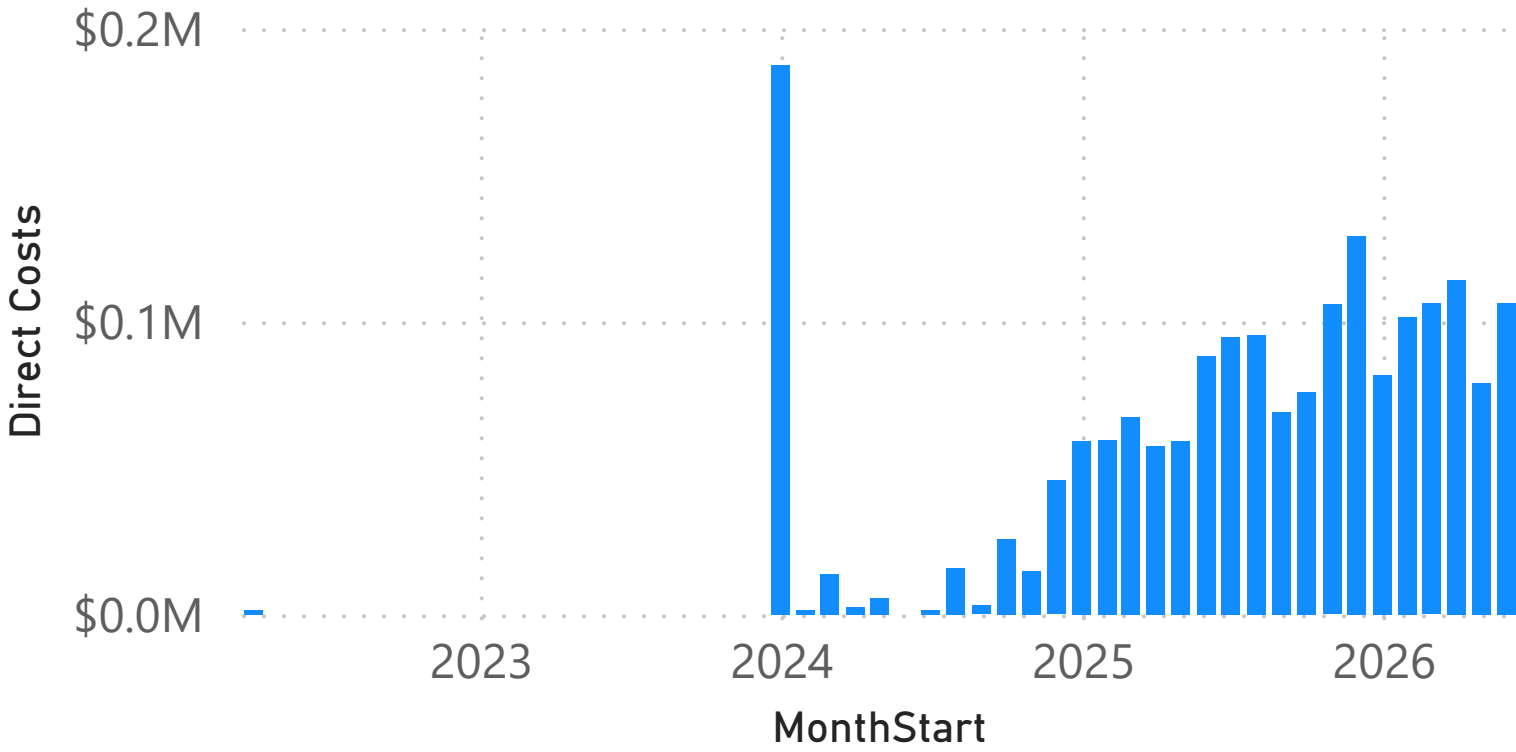

Committed and actual by cost code

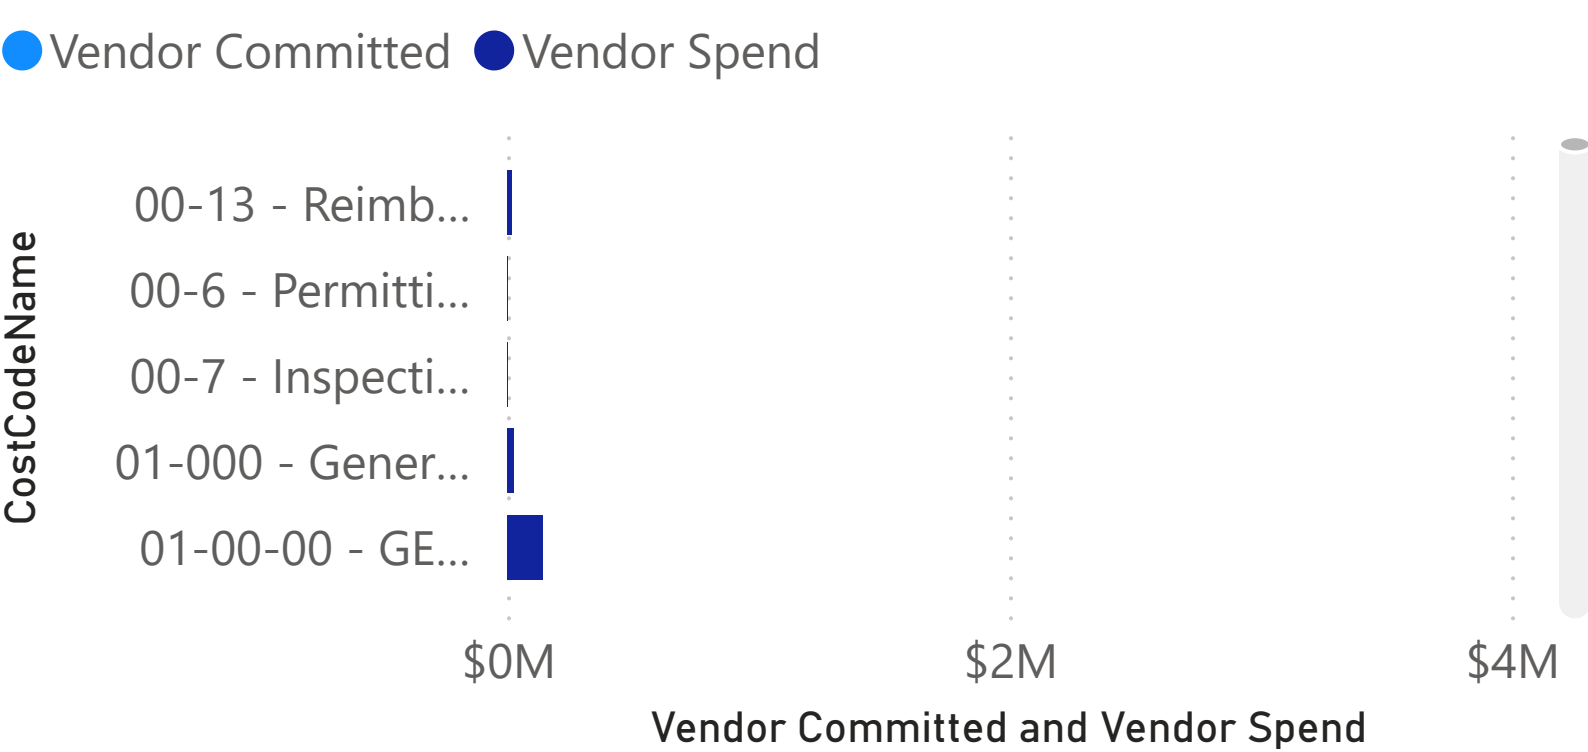

| AmountType                    | Actual       |                  | Committed    |                  | Total        |
|-------------------------------|--------------|------------------|--------------|------------------|--------------|
| VendorName                    | Vendor Spend | Vendor Committed | Vendor Spend | Vendor Committed | Vendor Spend |
| A York Cleaning Company, Inc. |              |                  |              | \$16,000         |              |
| A&L Cesspool                  |              |                  |              | \$600            |              |
| AAA                           | \$1,000      |                  |              |                  | \$1,000      |
| ABM Interiors                 | \$14,782     | \$2,209,470      | \$14,782     | \$2,209,470      | \$14,782     |
| AES Lighting Group            |              |                  |              | \$603,500        |              |
| AF Supply Corp.               |              |                  |              | \$43,124         |              |
| Affect                        | \$1,259,021  | \$1,000,000      | \$1,259,021  | \$1,000,000      | \$1,259,021  |
| AHC Appliances                |              |                  |              | \$51,307         |              |
| AirFlow Dynamics Inc          |              |                  |              | \$589,000        |              |
| Alba Services, Inc.           |              |                  |              | \$26,000         |              |
| Alejandro Camera              | \$2,667      |                  |              |                  | \$2,667      |
| Amazon                        | \$9,853      |                  |              |                  | \$9,853      |

| VendorName                    | TradeName        | City       | LicenseNumber |
|-------------------------------|------------------|------------|---------------|
| 11 Essex Street Realty LLC    |                  | New York   |               |
| A York Cleaning Company, Inc. |                  |            |               |
| A&L Cesspool                  |                  | New York   |               |
| ABC Environmental LLC         |                  | New York   |               |
| ABM Interiors                 |                  | Yonkers    |               |
| AES Lighting Group            |                  | Whippany   |               |
| AF Supply Corp.               |                  | New Jersey |               |
| Affect                        | Affect Build LLC | New York   |               |



# Vendor Insurance

Sourced from Procore's insurance records. **COVERAGE** (is there a certificate at all) and **CURRENCY** (is it in date) are counted separately - a vendor with no record and a vendor with a lapsed record both fail a single compliance flag and need different follow-up. Exempt vendors are counted apart from lapsed ones.

Coverage

Currency

251

23

245

105

105

0

Vendors On Project

Vendors With Insurance


Vendors Without Insurance

Certificates On File


Expired Certificates

Certificates Expiring Soon


Certificates by expiry status

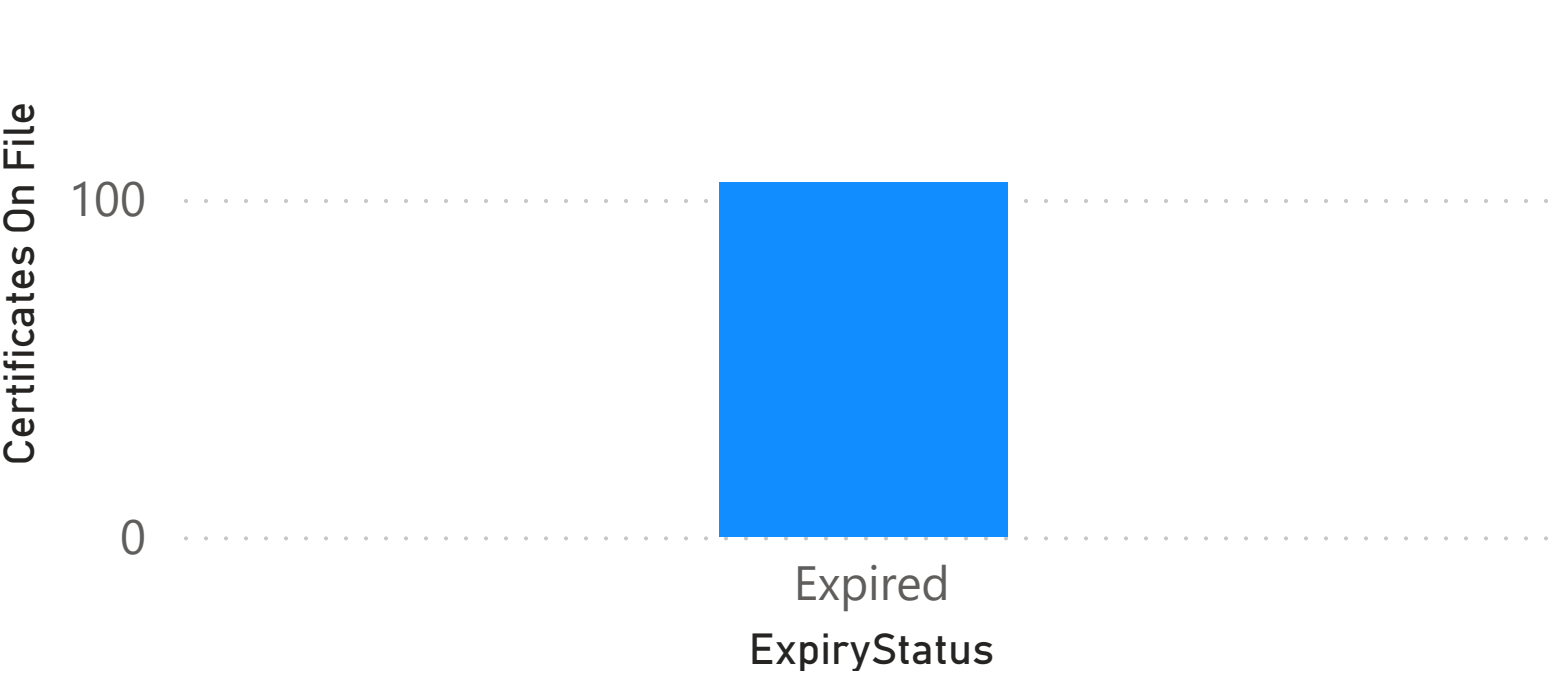

Certificates by type (Procore's free-text values, untidied)

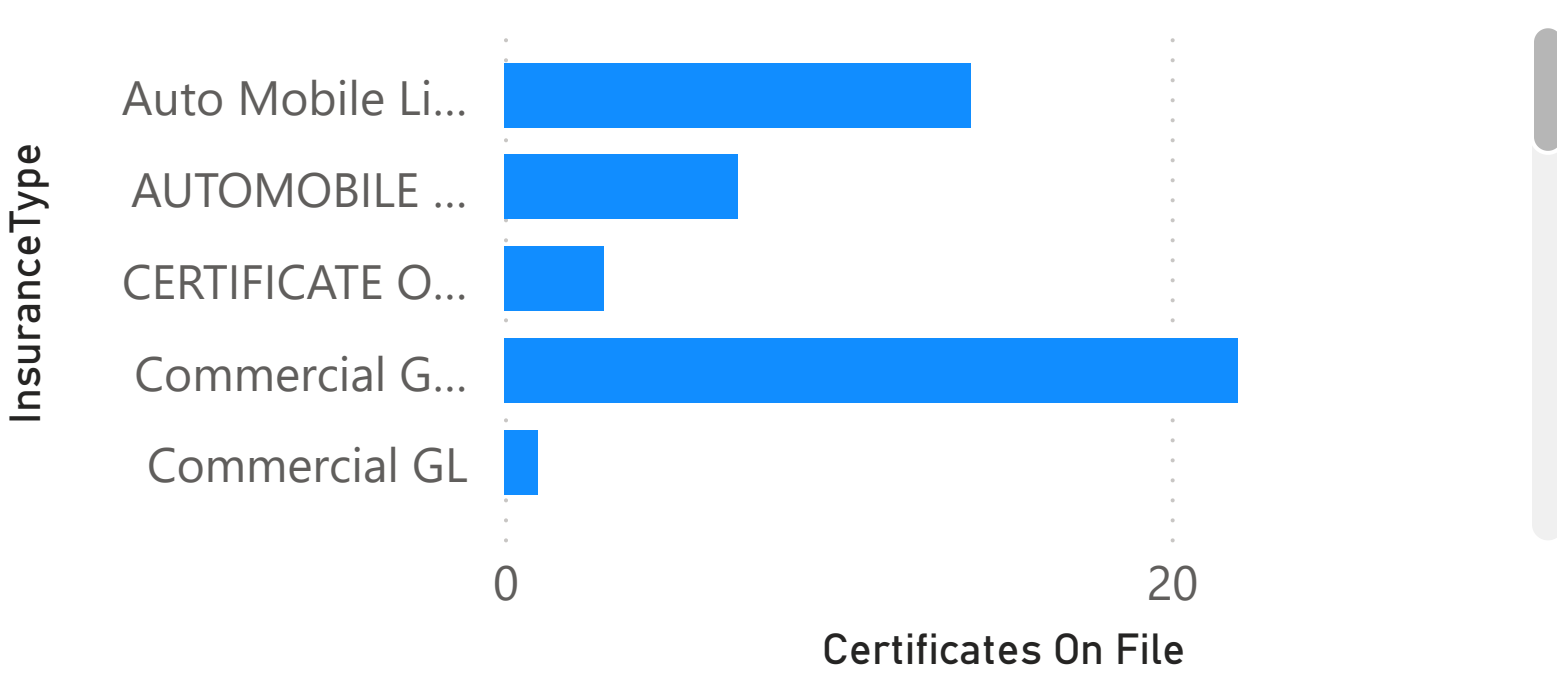

Lapsed vs in date vs exempt

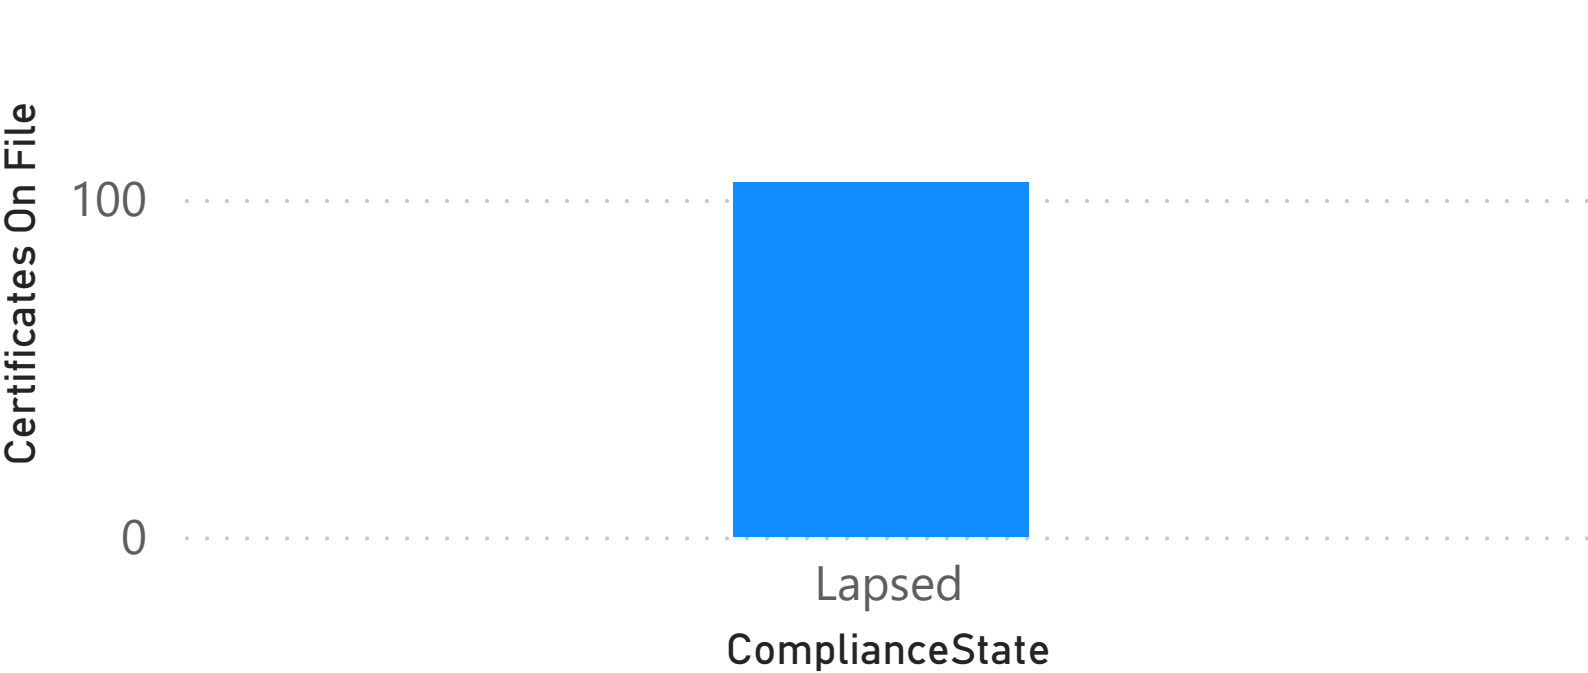

| VendorKey       | InsuranceType                      | Provider                           | PolicyNumber | ExpirationDate | ExpiryStatus | DaysUntilExpiry |
|-----------------|------------------------------------|------------------------------------|--------------|----------------|--------------|-----------------|
| 562949957487146 | Auto Mobile Liability              | Utica National Insurance Company   | 5438989      | 2024-04-13     | Expired      | -842            |
| 562949957487146 | CERTIFICATE OF LIABILITY INSURANCE | United Specialty Insurance Company | CPP5514601   | 2023-04-24     | Expired      | -1197           |
| 562949957487146 | Workers' Compensation Insurance    | Sirius America Insurance Company   | WC39748 02   | 2024-04-24     | Expired      | -831            |
| 562949957487167 | AUTOMOBILE LIABILITY               | Merchants Mutual Insurance Company | CAP1077243   | 2023-11-03     | Expired      | -1004           |
| 562949957487167 | Commercial General Liability       | Merchants Mutual Ins Co            | CTRI000121   | 2023-03-05     | Expired      | -1247           |
| 562949957487167 | Umbrella Liab Excess Liab          | Merchants Mutual Insurance Company | CUPI002790   | 2023-03-05     | Expired      | -1247           |
| 562949957487167 | Workers Comp & Employers Liability | Merchants Mutual Insurance Company | WCAI037746   | 2023-03-05     | Expired      | -1247           |

January 2015 - Dec...

Report Month Label

2026-08-03 06:06

Last Refresh

Current

Disposal Status



# Project Scorecard

Weights and bands are data (dim\_ScorecardWeight / dim\_ScorecardBand) - retune them without a code change. A category with no data scores BLANK,

ProjectName

(Blank)

MonthYear

(Blank)

0.26

Project Scorecard

59.0%

Scorecard Coverage %

0.44

Project Scorecard (Measured Only)

(Blank)

Client Satisfaction

| CategoryName         | Category Score | Category Band | Weight | Category Weighted |
|----------------------|----------------|---------------|--------|-------------------|
| Accounts Receivable  |                | Not measured  | 0.12   |                   |
| Cash Position        | 3              | >= 100%       | 0.12   | 0.120             |
| Change Orders        | 0              | > 60 days     | 0.08   | 0.000             |
| Completion Variance  |                | Not measured  | 0.15   |                   |
| Daily Reports        |                | Not measured  | 0.02   |                   |
| Observations         | 0              | >= 11 days    | 0.10   | 0.000             |
| Profitability        |                | Not measured  | 0.12   |                   |
| Safety Incidents     | 3              | 0             | 0.14   | 0.140             |
| Schedule Performance | 0              | >= 10%        | 0.15   | 0.000             |
| Total                |                | Not measured  |        |                   |

| CategoryName        | Score | BandLabel  |
|---------------------|-------|------------|
| Accounts Receivable | 0     | > 60 days  |
| Accounts Receivable | 2     | 45-60 days |
| Accounts Receivable | 3     | < 45 days  |
| Cash Position       | 0     | < 50%      |
| Cash Position       | 2     | 50-99%     |
| Cash Position       | 3     | >= 100%    |
| Change Orders       | 0     | > 60 days  |
| Change Orders       | 2     | 46-60 days |
| Change Orders       | 3     | <= 45 days |
| Completion Variance | 0     | >= 15 days |
| Completion Variance | 2     | 1-14 days  |
| Completion Variance | 3     | <= 0 days  |
| Daily Reports       | 0     | >= 5       |
| Daily Reports       | 2     | 2-4        |

WHY THIS DIFFERS FROM THE 0.59 IN THE WORKBOOK. Two scoring bands are wrong there: Schedule Performance uses 5/10 where the data is a fraction (0.05/0.10), so it always scored 3; Completion Variance never matched any band, so it always scored 0. On the sample project those two errors cancel exactly - which is why nobody noticed. On a project where they do not cancel, the workbook's score is wrong by the difference. The bands here are corrected (dim\_ScorecardBand). Affect decides when to switch the number reported to leadership.

# Source Coverage

A project missing from Sage reads as ZERO revenue everywhere - it does not error, it just looks like a project that never billed. Every project below appears exactly once; the status says what is missing.

1

Projects Fully Mapped

4

Projects Missing From Sage


17

Projects Missing From Outbuild

5.3%

Source Coverage %

Projects by coverage status



| ProjectName                                                | CoverageStatus                            |
|------------------------------------------------------------|-------------------------------------------|
| 11 ESSEX ST                                                | Missing from Outbuild - no milestones     |
| 1100 Fulton Street                                         | Missing from Outbuild - no milestones     |
| 337A & 337B West Broadway Rehabilitaion Work               | Missing from Outbuild - no milestones     |
| 360 Lexington 8th & 20th Floor                             | Fully mapped                              |
| 549 Munroe Av                                              | Missing from Outbuild - no milestones     |
| 64 MET OVAL PSC + 1410 MET STOREROOM                       | Missing from Outbuild - no milestones     |
| Boys & Girls Club                                          | Missing from Outbuild - no milestones     |
| City Harvest                                               | Procore only - no financials, no schedule |
| Embankment + Revetment Apartments 270 & 310 10th Street NJ | Missing from Outbuild - no milestones     |

| VendorName | IsInSage | HasNameMismatch |
|------------|----------|-----------------|
|------------|----------|-----------------|

Vendors below are expected to be mostly unmatched - a vendor invited to bid is not a vendor who was paid. What matters is a vendor WITH commitments and no Sage id.

| VendorName         | IsInSage | HasNameMismatch |
|--------------------|----------|-----------------|
| AES Lighting Group | True     | False           |
| AF Supply Corp.    | True     | False           |

| DivisionCode | CostCode | HasUnparseableCode |
|--------------|----------|--------------------|
|--------------|----------|--------------------|

| DivisionCode | CostCode | HasUnparseableCode |
|--------------|----------|--------------------|
| 1-1000       | True     |                    |
| 1-10001      | True     |                    |
